CORPORATE AND FINANCIAL COMMITTEE 3. 8. 2012

3. EARTHQUAKE FINANCIAL REPORT FOR MAY 2012

General Manager responsible:	Paul Anderson – General Manager, Corporate Services DDI 941 8528		
Officer responsible: Diane Brandish – Corporate Finance Manager			
Author:	Paul Anderson – General Manager, Corporate Services		

PURPOSE OF REPORT

- 1. The purpose of this report is to provide an update to the Council on financial matters relating to the earthquakes, as at 31 May 2012.
- 2. The report includes an overview on the expected overall financial impact of the earthquakes on the Council.

EXECUTIVE SUMMARY

- 3. Attached are appendices showing summaries of:
 - May Earthquake net cost and 2011/12 forecast (**Appendix 1**)
 - Earthquake life-to-date cost details (**Appendix 2**)
 - Earthquake overall cost forecast (**Appendix 3**)
 - Recoveries summary (**Appendix 4**).

Rebuild Costs

- 4. Expenditure of \$38.9 million was incurred in May, of which Stronger Christchurch Infrastructure Rebuild Team (SCIRT) costs amounted to \$24.9 million. SCIRT costs life-to-date now total \$241.5 million. Of this, \$78.7 million of work in progress was allocated in May across the specific areas of work as follows: \$49.8 million Wastewater; \$13.8 million Water Supply; \$7.8 million Pump Stations; \$6.7 million Roading; and \$0.6 million Stormwater.
- 5. Forecast expenditure for 2011/12 remains unchanged at \$286.8 million. This is \$59.0 million less than budget and relates to the facilities rebuild, with very little expenditure expected to occur this financial year while detailed engineering assessments are performed and Council approval for capital works is sought.

Emergency and Response Costs

- 6. Overall Emergency and Response costs increased by \$0.7 million in May. Wastewater response costs of \$4.1 million were incurred (an estimated 90% of which relate to ongoing repairs and silt removal following the December event), while a further \$4.4 million was largely made up of Rockfall (\$1.3 million), Roading (\$1.2 million), and costs associated with Council assets/facilities (\$0.9 million). Largely offsetting this however, were other Wastewater costs (Laterals, CCTV and pipe works) which have been identified as (and transferred to) capital.
- 7. The overall forecast Council net cost for emergency and response costs for 2011/12 is \$53.2 million, which is just slightly lower than last month's forecast (\$53.5 million).
- 8. Of the forecast net cost to Council of \$53.2 million, \$0.9 million is funded from the Earthquake Mayoral Relief Fund (part of Auckland City Council's contribution), the balance will be funded from borrowing.

Recoveries

- 9. Of the \$759.8 million response and rebuild costs (refer appendix 2) incurred, \$288.1 million in recoveries (refer Appendix 4) has been received. This includes \$139.3 million from the Crown and \$127.0 million from NZTA for both emergency and response, and rebuild costs.
- 10. During the month the following monies were received:
 - NZTA \$8.3 million for response rebuild costs
 - Crown \$24.3 million from CERA reflecting the Crown's share of SCIRT costs from 1 July 2012 until 31 December 2012.

3 Cont'd

Building / Infrastructure Improvement Allowance

11. The Building / Infrastructure improvement allowance is currently set at \$175 million by the Council. To date the following allocations have been approved, leaving a balance of \$157 million.

Description	Meeting Date	Value
Oxidation Ponds	25/08/2011	16,128,000
Temporary Stadium cost contribution Rugby League Park	08/09/2011	1,000,000
Fendalton Library and Service Centre	16/02/2012	190,000
Linwood Community Arts Centre	15/03/2012	35,884
Cowles Stadium	05/04/2012	480,000
Pump Station 37	05/04/2012	126,000

The 2012/13 Annual Plan includes a further \$79.3 million of allocation to the Major Facilities Rebuild Programme. This would leave a balance of \$77.7 million.

Do the Recommendations of this Report Align with 2009-19 LTCCP budgets?

12. Yes – there are none.

LEGAL CONSIDERATIONS

Have you considered the legal implications of the issue under consideration?

13. Yes – there are none.

ALIGNMENT WITH LTCCP AND ACTIVITY MANAGEMENT PLANS

14. Both service delivery and financial results are in direct alignment with the LTCCP and Activity Management Plans.

Do the recommendations of this report support a level of service or project in the 2009-19 LTCCP?

15. As above.

ALIGNMENT WITH STRATEGIES

16. Not applicable.

CONSULTATION FULFILMENT

17. Not applicable.

STAFF RECOMMENDATION

That the Committee recommend to the Council that it receive the report.

Appendix 1: Council net cost and 2011/12 forecast update as at 31 May 2012

	Actual month (\$m)				2011/12 net cost forecast			
	Cost Recovery Net				Current	Last	Change	
Infrastructure Rebuild								
Roading	6.1	4.5	1.5		26.0	26.4	(.4)	
Sewer	59.5	59.5	.0		-	-	-	
Water	13.8	13.8	.0		(.0)	-	(.0)	
Stormwater	2.1	1.5	.6		1.6	1.6	-	
SCIRT setup and overhead costs unallocated	()		(1.5.5)					
	(53.8)	(43.0)	(10.8)		-	-	-	
Total 2	27.7	36.3	(8.6)		27.5	28.0	(.4)	
2 Other Assets and Insured Costs:	21.1	30.3	(0.0)		21.5	20.0	(.+)	
Buildings and Facilities	.9	.2	.7		9.1	9.1	— —	
Sewer above-ground assets	.9 4.2	3.8	.7 .5		13.5	9.1 14.4	(0)	
Water above-ground assets	4.2 6.0	5.0 6.2			.1	14.4 -	(.9)	
Stormwater above-ground assets	0.0	.0	(.2) .0		- •'-		- ·'-	
Park Facilities	.0	.0	.0					
	-					-		
Council Buildings / Infrastructure improvement allowance		-	-		-	5.4	-	
Uninsured Assets (Parks, Stormwater) Insurance Excesses	.1	.0	.0		6.4	5.4	.9	
	-	-	-		-	-	.1	
Total	11.2	10.2	1.0		29.0	28.9	.1	
Emergency & Response Costs:								
Roading Emergency Work	1.2	.9	.3		6.3	6.4	(.1)_	
Welfare and other Emergency Work 3	(1.7)	(1.7)	(.0)		2.6	3.0	(.4)	
Other Response Costs	(1.1)_	()_	(.0)		2.0	0.0	()_	
4	5.6	1.2	4.4		9.4	5.8	3.6	
Roading Temp Maintenance Works	.1	.1	(.0)		4.1	4.2	(.1)	
Non-Roading Temp Maintenance Works								
5	(6.1)	(5.8)	(.3)		27.2	30.2	(3.1)	
Demolition Costs	.0	(.0)	.0		.1	.1	.0	
Rockfall	1.3	.7	.6		8.2	8.7	(.5)	
Increased Costs of Working	.1	.1	(.0)		(7.9)	(7.9)	(.0)	
Staff/Other internal costs charged to Emerg/Resp	.4	-	.4		8.7	8.2	.5	
Less costs budgeted in Council activities	(.3)	-	(.3)		(5.5)	(5.1)	(.4)	
Total	.7	(4.5)	5.2		53.2	53.5	(.3)	
Grand Total	39.6	42.0	(2.4)		109.7	110.4	(.6)	

Notes:

1) Reflects a \$78.7 million allocation of SCIRT costs across the infrastructure areas, partially offset by \$24.9 million of further SCIRT costs incurred in May.

2) Accrued recoveries exceed costs for the month due to the allocation of SCIRT costs. This has resulted in a more accurate estimate of accrued recoveries.

3) Reduction due to Wastewater below ground costs transferred to capital.

4) Majority of the month's expenditure is ongoing Wastewater below ground response costs. The \$4.4 million increase in net cost to Council includes a \$2.3 million adjustment to the accrued recoveries in the EOC area, which were previously overstated.

5) Reduction due to Wastewater below ground costs relating to Lateral, CCTV and pipe works transferred to capital.


Appendix 2: Life-to-date results as at 31 May 2012

	Life to Date (\$m)						
	Cost		Accrued	Recoveries			Balance
		LAPP (F)	LAPP (I)	DIA/CERA	NZTA	Other	Council
Infrastructure Rebuild							
Roading	7.4	-	-	-	5.5	-	1.9
Sewer	65.0	-	26.0	39.0	-	-	.0
Water	19.0	-	7.4	11.1	-	-	.5
Stormwater	19.0	-	3.2	11.4	-	-	4.4
SCIRT setup and overhead costs unallocated 1	162.8	-	32.6	48.8	48.8	-	32.6
Total	273.2	-	69.1	110.3	54.4	-	39.4
Other Assets and Insured Costs:							
Buildings and Facilities	9.0	2.4	-	.0	-	.0	6.6
Sewer above-ground assets	17.0	16.6	-	-	-	-	.4
Water above-ground assets	6.4	6.2	-	-	-	-	.2
Stormwater above-ground assets	.0	.0	-	-	-	-	.0
Park Facilities	-	-	-	-	-	-	-
Council Buildings / Infrastructure improvement							
allowance	-	-	-	-	-	-	-
Uninsured Assets (Parks, Stormwater)	2.1	.2	-	-	.3	-	1.6
Insurance Excesses	8.0	-	-		-	-	8.0
Total	42.5	25.4	-	.0	.3	.0	16.8
Emergency & Response Costs:							
Roading Emergency Work	92.9		2.2	3.3	65.9	.0	21.4
Welfare and other Emergency Work	65.9		12.5	52.8	-	.0	.6
Other Response Costs	66.3	20.4	-	18.5	1.8	4.8	20.8
Roading Temp Maintenance Works	31.8		.0	.0	22.6	(.0)	9.1
Non-Roading Temp Maintenance Works	149.7	.0	29.6	91.1		.6	28.4
Demolition Costs	10.5	-	-	6.2		.1	4.2
Rockfall	18.3	-	-	7.3	1.6	.0	9.5
Increased Costs of Working 2	(1.8)	2.8	-	-	-	5.3	(9.9)
Staff/Other internal costs charged to Emerg/Resp	47.6	-	-	-	-	-	47.6
Less costs budgeted in Council activities	(36.9)	-	-	-	-	-	(36.9)
Total	444.2	23.2	44.3	179.1	91.9	10.8	94.8
Grand Total	759.8	48.6	113.5	289.5	146.6	10.8	150.9

Notes:

1) 2) SCIRT setup and overhead costs will be allocated over infrastructure assets upon job completion.

Credit due to extra tankered waste revenue and Civic Offices rental rebate.

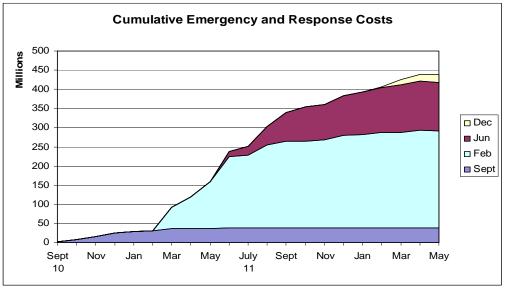

Appendix 3: Life forecast

	Life forecast (\$m)						
	Cost			Recoveries			Balance
		LAPP (F)	LAPP (I)	DIA/CERA	NZTA	Other	Council
Infrastructure Rebuild							
NZTA-subsidised roading (excl State Highways)	842.4	-	-	-	699.2	-	143.2
Non-subsidised roading (excl State Highways)	164.3	-	-	-	-	-	164.3
Sewer	694.0	-	277.6	416.4	-	-	-
Water	140.1	-	56.0	84.1	-	-	-
Stormwater	66.5	-	26.6	39.9	-	-	-
LAPP liability limitation	-	-	(196.2)	-	-	-	196.2
SCIRT setup and overhead costs unallocated	-	-	-	-	-	-	-
Total	1,907.3	-	164.1	540.4	699.2	-	503.7
Other Assets and Insured Costs:							
Buildings and Facilities	463.4	452.8	-	-	-	-	10.6
Sewer above-ground assets	103.1	103.1	-	-	-	-	-
Water above-ground assets	26.6	26.6	-	-	-	-	-
Stormwater above-ground assets	.9	.9	-	-	-	-	-
Park Facilities	4.0	4.0	-	-	-	-	-
Council Buildings / Infrastructure improvement allowance	175.0	-	-	-	-	-	175.0
Uninsured Assets (Parks, Stormwater)	87.2	-	-	-	-	8.0	79.2
Insurance Excesses	23.9	-	-	-	-	-	23.9
Total	884.1	587.4	-	-	-	8.0	288.8
Emergency & Response Costs:							
Roading Emergency Work	87.8	-	2.2	3.3	63.9	.0	18.3
Welfare and other Emergency Work	73.9	-	13.2	55.0	-	.0	5.8
Other Response Costs	51.4	22.4	-	11.8	-	3.2	14.0
Roading Temp Maintenance Works	65.0	-	.0	-	41.0	.0	24.0
Non-Roading Temp Maintenance Works	220.4	-	28.7	125.4	-	11.4	54.9
Demolition Costs	10.5	-	-	5.9	-	.1	4.5
Rockfall	55.0	-	-	-	1.2	-	53.8
Increased Costs of Working Staff/Other internal costs charged to	6.0	3.0	-	-	-	-	3.0
Emerg/Resp	11.7	-	-	-	-	-	11.7
Less costs budgeted in Council activities	-	-	-	-	-	-	-
Total	581.6	25.4	44.2	201.3	106.1	14.7	190.0
Grand Total	3,373.1	612.8	208.2	741.7	805.3	22.7	982.4

This table shows the same information as presented in the 2012/13 Draft Annual Plan (p42), with an expanded view of the forecast recoveries.

Appendix 4: Recoveries Summary

\$(Monthly reco m) All Figures a	overies summa re GST Exclus		as at	31/05/2012		
Rebuild	Total	Crown	NZTA	LAPP (I)	LAPP (F)	Other	Notes
Cost incurred to date	315.7						
Recoveries accrued	259.5	110.3	54.7	69.1	25.4	0.0	
Recoveries received	67.5	24.3	38.2	0.0	5.0	0.0	
Recoveries claimed but unpaid	0.0	0.0	0.0	0.0	0.0	0.0	
Balance unclaimed to date	192.0	86.0	16.5	69.1	20.4	0.0	
Significantly Damaged Buildin	gs (No rebuild o	ost incurred b	out indem	nity recove	ry claimed)		
Recoveries accrued	53.6	0.0	0.0	0.0	47.4	6.3	Overcap properties claim from EQC (\$6.3m)
Recoveries received	55.8	0.0	0.0	0.0	34.9	20.9	
Recoveries claimed but unpaid	12.5	0.0	0.0	0.0	12.5	0.0	
Balance unclaimed to date	-14.7	0.0	0.0	0.0	0.0	-14.7 *	to be recognised
Emergency and Response							
Cost incurred to date	483.0						
Recoveries accrued	341.3	179.1	91.9	44.3	20.4	5.5	
Recoveries received	220.6	115.0	88.8	14.1	0.1	2.6	
Recoveries claimed but unpaid	75.9	72.8	0.0	3.1	0.0	0.0	
Balance unclaimed to date	44.8	-8.7 (1)	3.1	27.1	20.3	2.9 (2) (1) Demolitions accrued at 60% but claimed at 100% (2) Ferrymead Bridge contract works cover bal and EQC
Increased Costs of Working							
Cost incurred to date	3.1						Excluding Office Accom due to Civic Building net rebate
Claims to be lodged (estimate)	2.8				2.8		
